

AXONOMETRIC VIEW (not to scale)

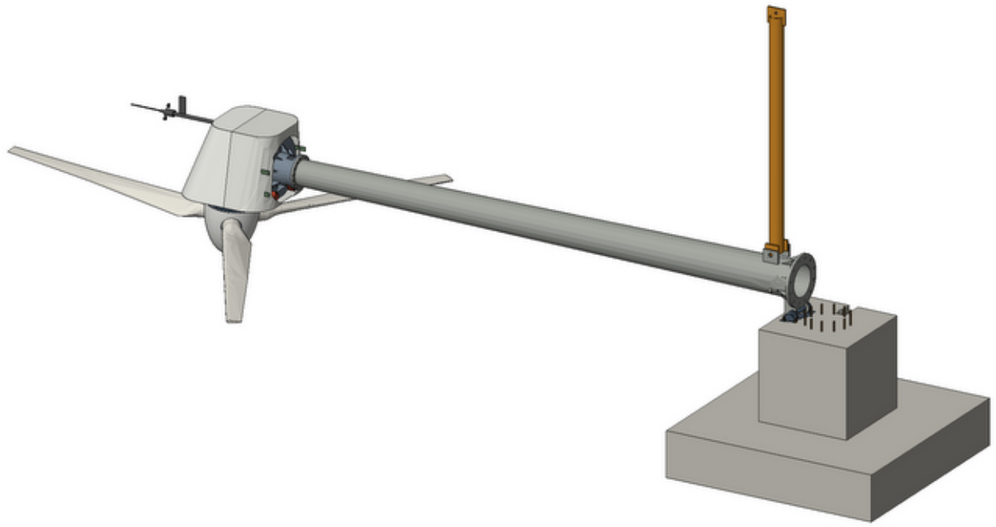

| Item | Value |
|---|---|
| Gin pole | 3.0 m, fixed square to the tower on its lugs |
| Peak line pull | ≈ 38 kN (wind ≤ 10 m/s) |
| Bridle | 2 × wire rope Ø16 6×36 IWRC to the top flange lugs |
| Pull line | Ø16 wire rope, winch ≥ 50 kN with 1:2 block |
| Ground anchor | screw anchors or concrete block, ≥ 80 kN at 6 m |
| Alternative | truck crane ≥ 3 t at 9 m reach (lift by the top flange) |

TILT-UP (tower horizontal on the hinge, head fitted, rotor locked)

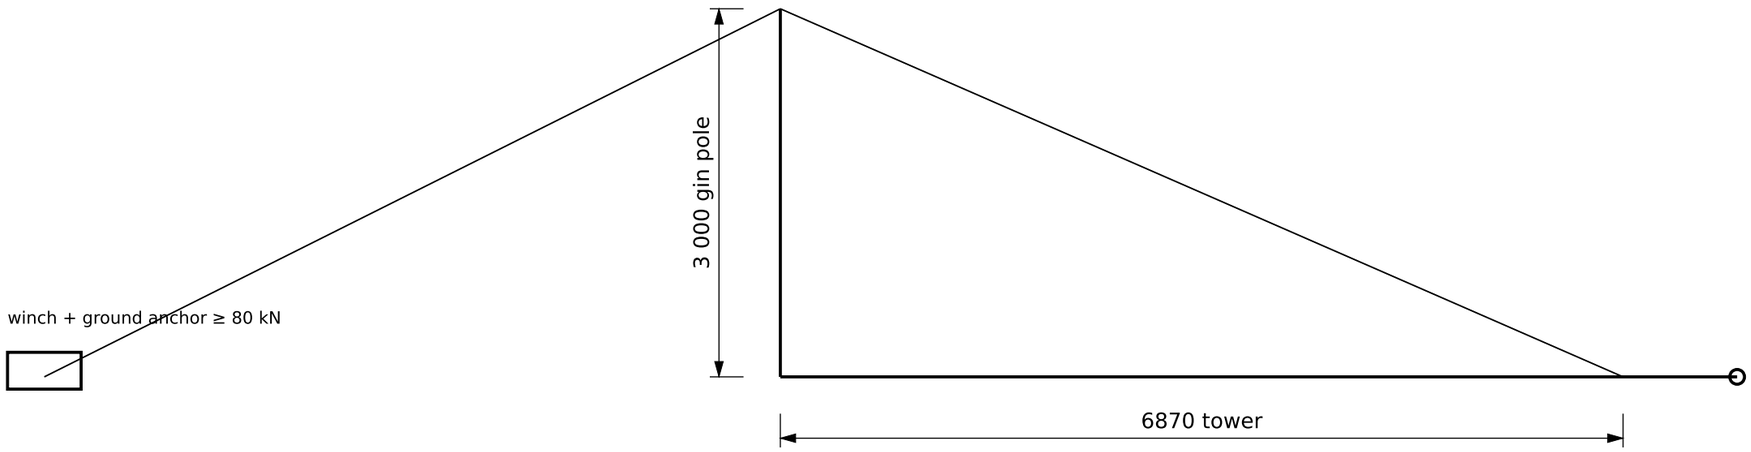


**NOTES**

1. Two people + winch operator; wind below 10 m/s; nobody inside the fall zone (1.5 × tower + rotor). Rotor locked with pin NP1-320, blade B1 pointing up away from the ground.
2. Lower the tower the same way for service; support the head on a trestle 1.0 m high so the lower blade clears the ground.
3. After erection: fit base nuts and torque (NS6-900), remove the gin pole, keep it with the site kit.

Dimensions mm · ISO 2768-mK · ISO 8015 · first angle projection · edges broken 0.5 unless stated · NOT CHECKED: prototype release only after review

**6 kW WIND TURBINE S6 (ICELAND) · FIXED PITCH, STALL CONTROL**

# GIN POLE AND TILT-UP RIGGING (ERECTION TOOL)

| DRAWING NO. | REV / DATE | SCALE (A3) |
|---|---|---|
| NS6-420 | B · 2026-11-06 | 1:50 |
| MATERIAL | MASS (CALC.) | DRAWN / CHECKED |
| S355 tube 168.3 × 6.3, plates 25 | 94 kg | Claude / not checked |
